PHASE 0 · AGENT CODE (LOCAL) — RUNS ALONE

Phase 0·Code — Setup and foundation (runs alone)

You can show after it: Sign up with email or Google → "Setting up your demo trucks..." → Home with 6 trucks, 1 trip on the road, problems and activity → tap हिंदी and everything (labels and demo data) is in Hindi → Settings saves costs.

RUN WITH
Agent Code — Claude desktop app, local (Account 1)

BRANCH
`main`

TIME · MODEL
≈ 3 h · Opus (Sonnet if usage is low)

Starts after	Runs at the same time as	Builds (Architecture section 8)
Repository with the docs committed	nothing — runs alone	F1 Project setup, database, sample data F2 Sign-in and accounts F3 Design system, Hindi button and shared helpers F4 App shell F5 Home (dashboard) F6 Settings

1. What this phase owns

Everything (it creates the project): root configs, `src/app`, `src/lib`, `src/types`, `src/i18n`, `src/components`, `src/features/{home,auth,settings}`, `supabase/functions/_shared`, `public/brand`, `public/icons`, `CLAUDE.md`, `docs/PROGRESS.md`, `docs/DECISIONS.md`.

2. Already built when you start

- Only the docs, `supabase/spareway_database.sql`, Vansh's CSVs in `data/pois/` and Bhavya's logo in `public/brand/`.

Read before planning: CLAUDE.md, docs/PROGRESS.md, the Plan PDF (sections 0, 1, 4 and your features in 8), Design System sections all (read fully), Engineering Reference sections 1, 2, 5, 7, 10, 11, 12, 13.

3. Start the session

1. Open the **Claude desktop app** (Account 1) → **Code** → **Local** → folder `spareway`.
2. New session, **Plan mode**, model as shown, paste the prompt.


```
You are Agent Code (local, with the Supabase MCP) for Spareway. Start Phase 0·Code. Read docs/Spareway_01_Plan_Architecture_and_Spec.pdf, docs/Spareway_02_Design_System.pdf and docs/Spareway_03_Engineering_Reference.pdf (all pages, in parts) and docs/phases/Phase0_Code_Setup_and_Foundation.pdf. Also read CLAUDE.md and docs/PROGRESS.md if they exist. Work on branch main. Ask me your questions first, then show your plan. Do not write code before I approve the plan.
```

4. Questions Claude must ask first

1. Is the Supabase MCP connected (`/mcp` → supabase authenticated)? If not, I'll give you SQL for the SQL Editor.
2. Are Google sign-in and Brevo email ready in Supabase? (Same code either way; decides what I can test today.)
3. Default language for a new visitor: English (default) or Hindi?
4. Is the logo in `public/brand/` final?

5. Build plan (in this order)

1. **Rules files**: CLAUDE.md (Engineering Reference 12.1), PROGRESS.md (one section per phase part), DECISIONS.md.
2. **Scaffold** (F1): Vite + React + TS, every package, configs, scripts, `.env.example`; build works without env.
3. **Database** (F1): 3 migrations with MCP, POI SQL from the CSVs, generate `database.ts`, run `get_advisors`.
4. **Contracts** (F1): domain.ts, modules, slots (Engineering Reference 1.2), router, query keys, errors.
5. **Design system + Hindi** (F3): tokens, fonts, components, i18n with `common` + `data` namespaces, Hindi demo dictionary (Engineering Reference 7.6), alert/activity templates, LanguageButton, MapView.
6. **Sign-in** (F2): AuthProvider, guards, bootstrap + seed, all auth pages.
7. **Shell + Home + Settings** (F4, F5, F6).
8. **Cloud check**: rename `.env.local` temporarily and run `npm ci && npm run check && npm run build` exactly as the cloud will; restore it.
9. Phase 0 runs alone, so it commits straight to `main`: small commits, push, then tag `v0` when the Verify list passes.

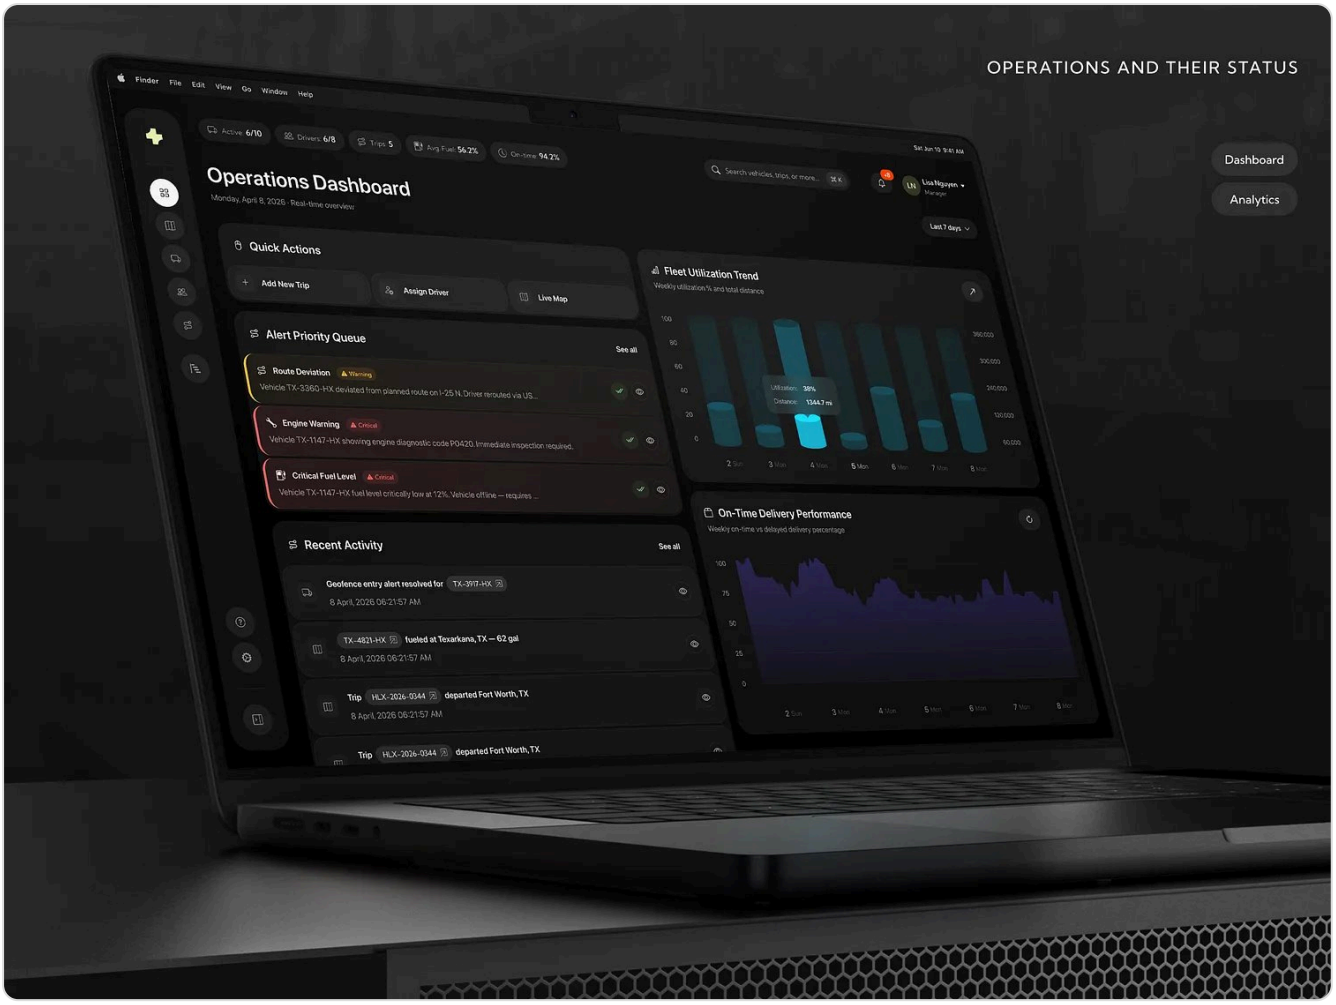

Haulix reference 1 — Operations Dashboard — Home uses this look, simplified (Design System 7.3).

6. Check before saying done

- ☐ `npm run check` and `npm run build` pass with zero errors.
- ☐ Fresh signup (email) → demo trucks → Home shows Trucks working 3 of 6, Trips on the road 1, Problems 4.
- ☐ Google sign-in works (if set up); forgot password always shows the same message; wrong password shows the plain message.
- ☐ Tap हिंदी: every label, the demo place/cargo/truck names and all problems/activity lines are Hindi; tap English: back. Choice kept after reload.
- ☐ Second account sees only its own data.
- ☐ 375 px phone layout, low-data toggle, Design System checklist (section 13).
- ☐ Every new screen tested with the Hindi button (labels + demo data).
- ☐ Design System section 13 check done.

7. Hand-off

1. Update the Phase 0·Code section of `docs/PROGRESS.md` (Engineering Reference 12.2): built, how to show it, open points.
2. Add assumptions to `docs/DECISIONS.md`.
3. Push `main`, tag `v0`, tell the user “Phase 0 done — start Phase 1 on both agents”.
