PHASE 1 · AGENT CODE (LOCAL)

# Phase 1·Code — Trucks, trips and cargo

You can show after it: Add a truck from a preset, create a trip with 3 drops, add cargo (demo trip shows 104 units), open the Load plan step and see the truck packed in 3D, activate it.

| RUN WITH | BRANCH | TIME · MODEL |
|---|---|---|
| Agent Code — Claude desktop app, local (Account 1) | `code/phase1-trucks-trips` | ≈ 3 h · Sonnet |

| Starts after | Runs at the same time as | Builds (Architecture section 8) |
|---|---|---|
| Phase 0 (tag v0) | 1·Git — Packing engine, 3D load plan, map style | F7 Trucks<br>F8 Trips and stops<br>F9 Cargo list |

## 1. Your lane and the other agent's lane

| | You — 1·Code | Other agent — 1·Git |
|---|---|---|
| Builds | F7 Trucks<br>F8 Trips and stops<br>F9 Cargo list | F10 Packing engine<br>F11 3D load plan<br>F12 Dark map style |
| Writes only in | `src/features/{trucks,trips,cargo}`, `supabase/sql/phase1code_*.sql`. | `src/features/load-planner`, `public/map`, `tools/map-preview.html`. |

**Never touch:** `src/features/load-planner`, `public/map` (Agent Git). Shared core files from Phase 0. Need something from the other lane? Use the fallback in your build plan or write a CONTRACT CHANGE REQUEST (Engineering Reference 12.4).

## 2. Already built when you start

- Project, database (+ real POIs), contracts, module + slot system, router.
- Sign-in pages, accounts, demo trucks for every new company.
- Design system incl. Hindi button, `td()` demo-data translation, NextStepCard, StepTabs, BigTile, MapView.
- Shell (rail / bottom tabs, top bar with Hindi button, bell, avatar menu), Home with slots `home.actions` + `home.widgets`, Settings with slot `settings.sections`.

**Read before planning:** CLAUDE.md, docs/PROGRESS.md, the Plan PDF (sections 0, 1, 4 and your features in 8), Design System sections 2–6, 7.4–7.6, 13, Engineering Reference sections 1, 2, 3, 7, 8, and the code in `src/app`, `src/components/common`, `src/types/domain.ts` and the `index.ts` of features you use.

## 3. Start the session

1. Open the **Claude desktop app** (Account 1) → **Code** → **Local** → folder `spareway`.
2. New session, **Plan mode**, model as shown, paste the prompt.


```
You are Agent Code (local, with the Supabase MCP) for Spareway. Start Phase 1·Code. Read docs/Spareway_01_Plan_Architecture_and_Spec.pdf, docs/Spareway_02_Design_System.pdf and docs/Spareway_03_Engineering_Reference.pdf (all pages, in parts) and docs/phases/Phase1_Code_Trucks_Trips_and_Cargo.pdf. Also read CLAUDE.md and docs/PROGRESS.md if they exist. Work on branch code/phase1-trucks-trips (create it from main). Ask me your questions first, then show your plan. Do not write code before I approve the plan.
```

## 4. Questions Claude must ask first


1. OK to offer typical Indian truck size presets labelled “typical — check your truck”?
2. Delivery times for stops: optional (default) or required?
3. Trip steps order: Cargo · Load plan · Loader · Route · Extra loads · Earnings — OK?

## 5. Build plan (in this order)

1. **Trucks** (F7) incl. board view, form with presets, truck page with tabs + `truck.tabs`.
2. **Trips** (F8): list, 3-step new trip, trip page with StepTabs + NextStepCard + slots `trip.steps`, `trip.actions`; hubs list.
3. **Cargo list** (F9) as trip step 1, add-item sheet, bars, realtime, slot `cargo.addMethods`; quick button New trip.
4. Tests, Hindi for every string, push.

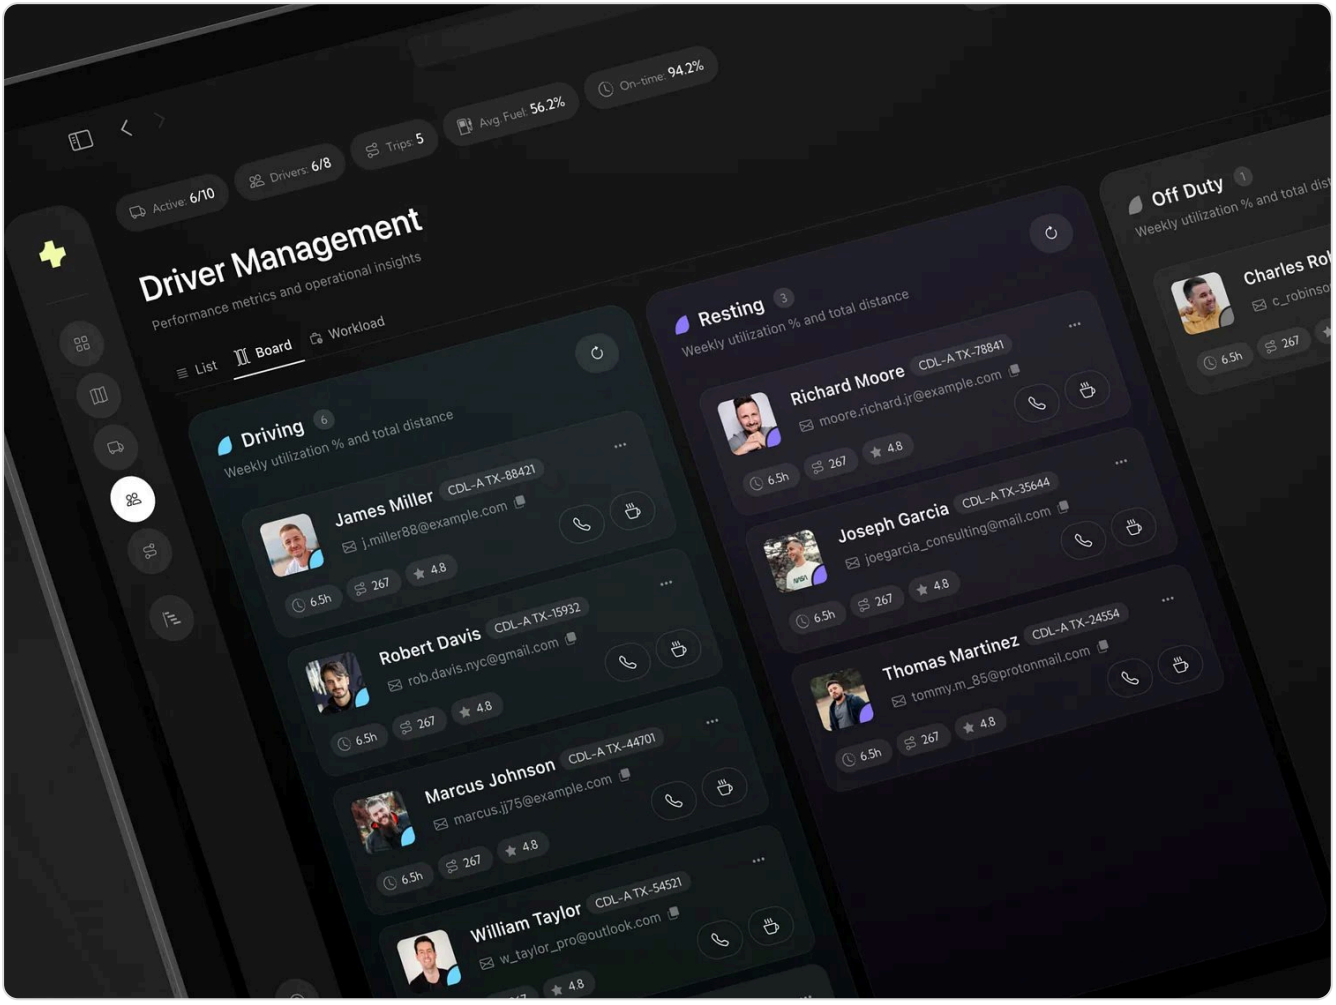


**Haulix reference 7 — Board view (columns by status) with person cards** — board view for Trucks and Trips.

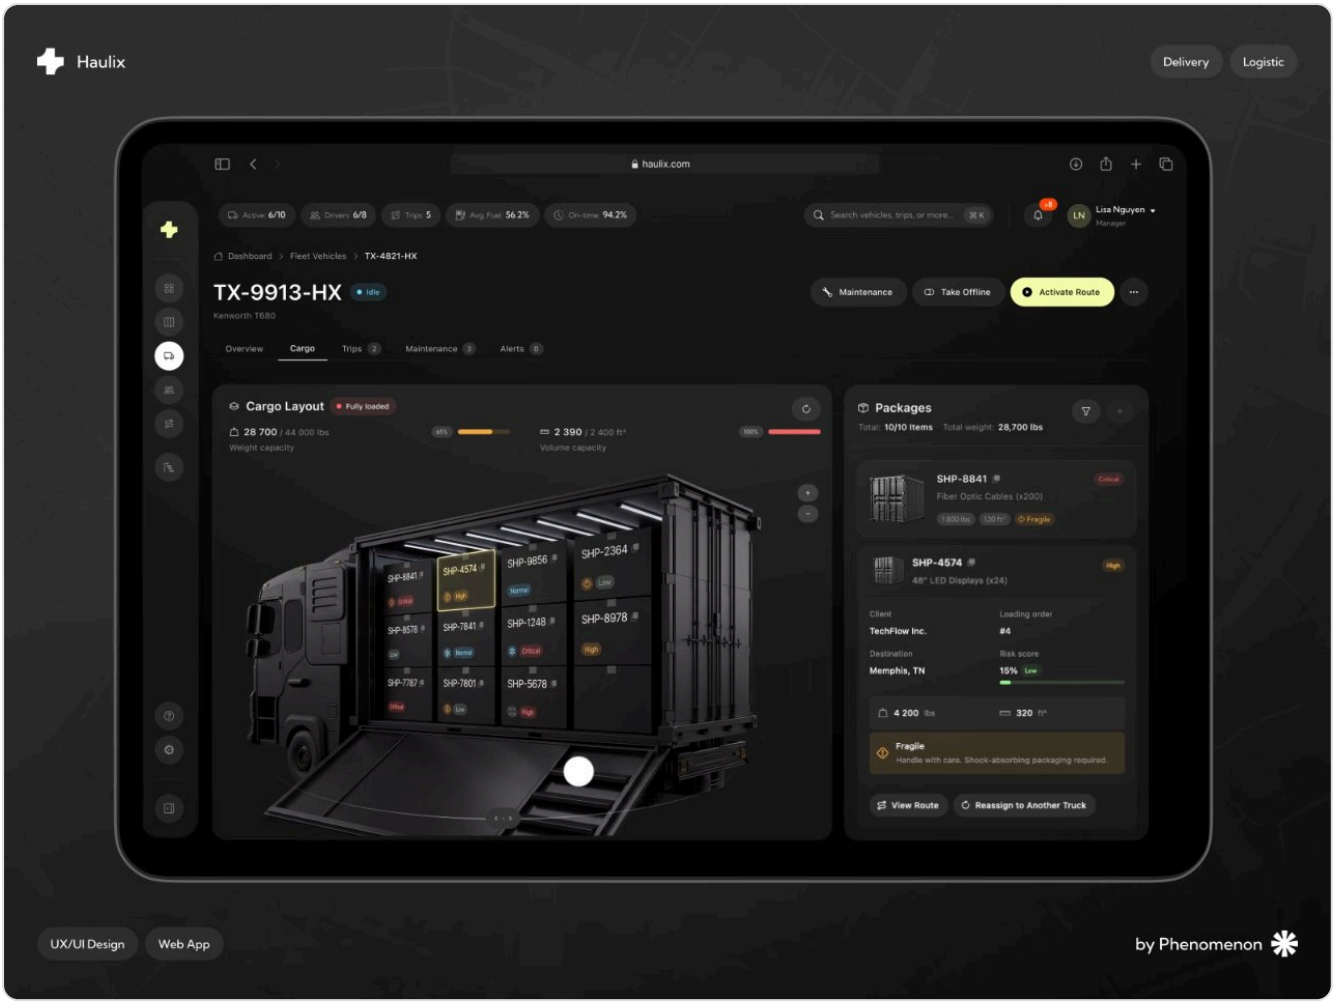


**Haulix reference 4 — Vehicle detail with 3D truck Cargo Layout + Packages detail** — truck page header and tabs.

## 6. Check before saying done

- ☐ `npm run check` and `npm run build` pass with zero errors.
- ☐ Edit MP09 HG 4821 in feet → saved 975/243/243 cm; add a truck from the 32 ft MXL preset.
- ☐ New trip Indore → Pune with 2 drops appears in Trips and activity.
- ☐ Demo trip Cargo: 104 units, 2,638 kg, bars ≈ 18% weight / 34% space.
- ☐ Hindi on every new screen; phone layout; Design checklist.
- ☐ Every new screen tested with the Hindi button (labels + demo data).
- ☐ Design System section 13 check done.

## 7. Hand-off

1. Update the Phase 1·Code section of `docs/PROGRESS.md` (Engineering Reference 12.2): built, how to show it, open points.
2. Add assumptions to `docs/DECISIONS.md`.
3. Push `code/phase1-trucks-trips` (do not merge to main).
4. Tell the user “Phase 1·Code ready to merge” + the 3 most important things to check.

## 8. Merge session (fresh Agent Code session, after both parts say “ready to merge”)

```
You are Agent Code. Merge Phase 1: merge origin/code/phase1-trucks-trips and then
origin/git/phase1-load-plan into main (Engineering Reference 11). Apply any
supabase/sql/phase1git_*.sql with the MCP, regenerate src/types/database.ts, run npm run
check and npm run build after each merge, then run the "Code must verify" list for Phase
1·Git in the real app (laptop + phone, English + Hindi) and fix small integration issues
(note them in DECISIONS.md). Report, then push main and tag v1.
```

- Merge `code/phase1-trucks-trips`, then `git/phase1-load-plan`; plan the demo trip for real and activate it; check map style loads; tag `v1`.
- After the tag, start Phase 2 on both agents from the new main.
